




2020 Street Improvements Northeast Area (Contract 20-101) Construction Updates August 10, 2020

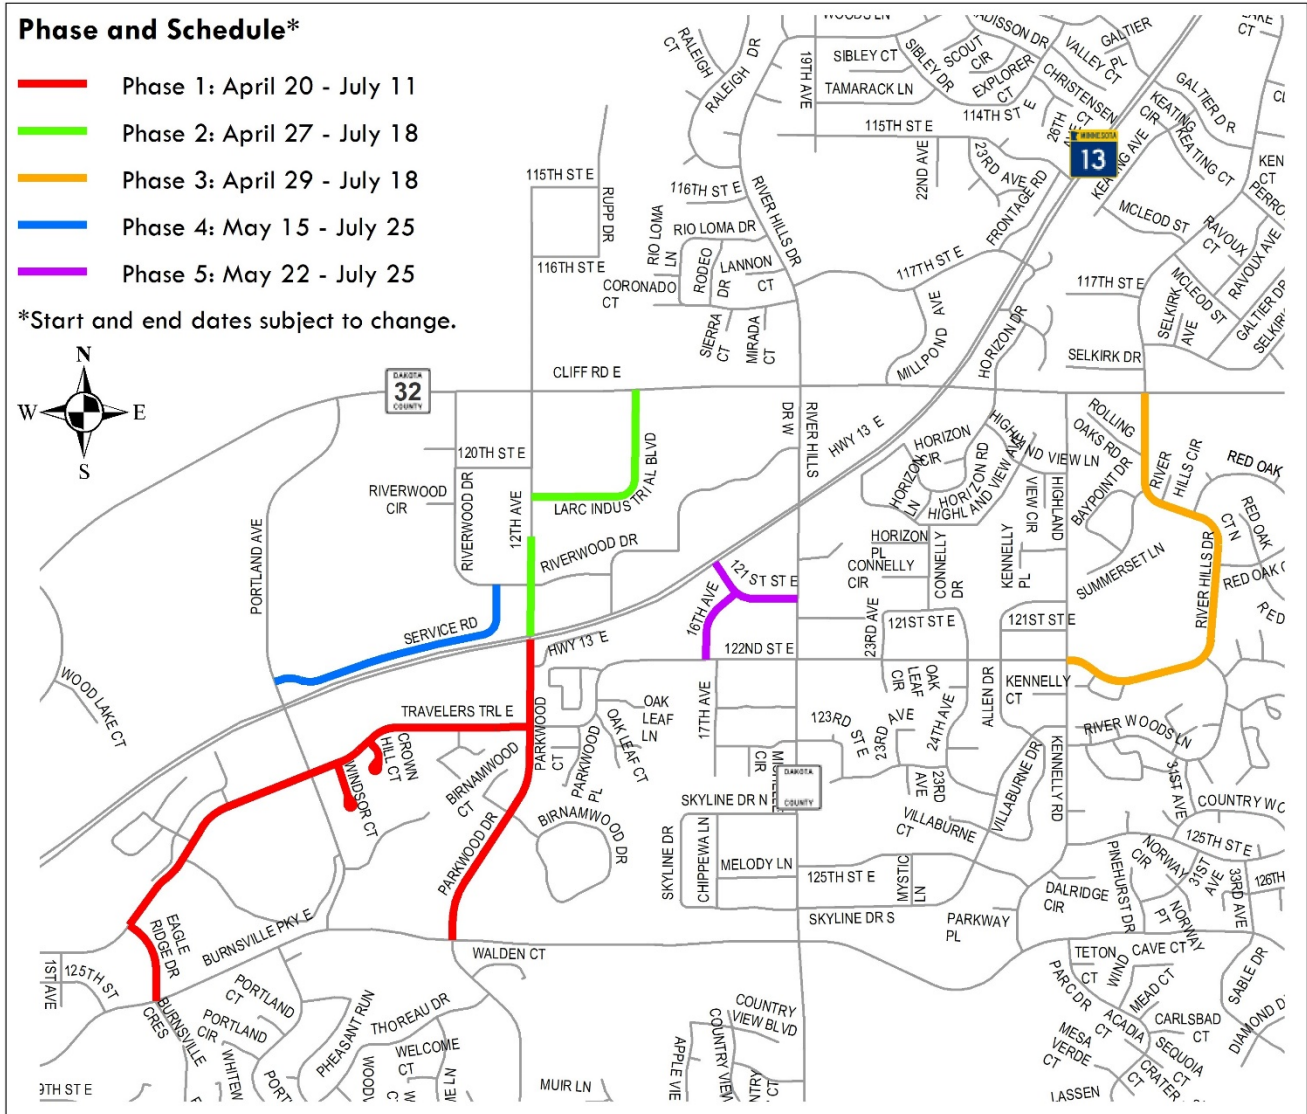

Date Saved: 7/2/2020 1:58:30 PM

Phase 1

Updates for the week of August 10-15, 2020:

- Finish replacing street signs
- Start re-work and seeding of weedy and uneven boulevards

Looking ahead to the week of August 17-22, 2020:

- Finish re-work and seeding of weedy and uneven boulevards

Phase 2

Updates for the week of August 10-15, 2020:

- Finish replacing street signs

Looking ahead to the week of August 17-22, 2020:

- Cleaning up site

Phase 3

Updates for the week of August 10-15, 2020:

- Finish replacing street signs

Looking ahead to the week of August 17-22, 2020:

- Cleaning up site

Phase 4

Updates for the week of August 10-15, 2020:

- Finish replacing street signs

Looking ahead to the week of August 17-22, 2020:

- Cleaning up site

Phase 5







Updates for the week of August 10-15, 2020:

- Finish replacing street signs

Looking ahead to the week of August 17-22, 2020:

- Cleaning up site

2020 Street Improvements Northeast Area (Contract 20-101) Estimated Schedule by Phase*

	 Start	 Utilities	 Curb	 Grading/Paving	 Restoration	 Complete
Phase 1	Apr 20	Apr 24 – May 8	Apr 30 – May 15	May 4-20	May 18 – Jul 11	Jul 11
Phase 2	Apr 24	May 5-8	May 26 – Jun 23	Jun 29 – Jul 2	Jun 22 – Jul 18	Jul 18
Phase 3	Apr 29	May 5-22	May 26 – Jun 4	May 19 – Jun 18	Jun 25 – Jul 18	Jul 18
Phase 4	May 15	May 18-21	May 28 – Jun 26	Jun 15 – Jul 11	Jul 13-25	Jul 25
Phase 5	May 22	May 26 – Jun 12	Jun 22-27	Jun 30 – Jul 11	Jul 13-25	Jul 25

*Projected dates are subject to change based on weather and contractor operations.

Contact City Inspector Cody Pietz at 952-356-6839 or cody.pietz@burnsvillemn.gov for more information

Subscribe to email and text message updates!

Visit www.burnsvillemn.gov/roadwork and click the “Subscribe” button to sign up for email and/or text message updates.



Subscribe
